

Lehi High School Rebuild Update

Overview: In the 2016 ASD bond election, Lehi High School was approved to undergo the final phases of a total rebuild. The project began this school year, and a multi-phase plan for the rebuild has been approved to be completed over the next three years. Considerations for the phasing of the rebuild included future enrollment projections, curriculum and program improvements, and the need to maintain all comprehensive high school programs throughout the project. Each phase of the project is described in greater detail below.


Phase I: This phase began March 1, 2018 and includes: relocation of the existing 18 room satellite, demolition of the existing north classroom wing, demolition of the media and counseling centers, and construction of a new vocational building and boiler plant (see site map below).

The satellite has been relocated to the north end of the campus and will accommodate the media center, TV/Video production, Photo Labs, a computer lab, and other classrooms during the construction period.

Demolition of the north classroom wing, media center, and counseling center is anticipated to be completed summer, 2018. This allows us to accelerate the overall timeline, saving time and resources in future phases. This area of the campus will house the new athletic facilities to be constructed in phase II.

A partial demolition of the existing vocational building will allow for construction of a new boiler plant in preparation for phase II.

The new vocational building is being constructed on the southeast end of the campus on the former site of the tennis courts. It will include: two Agricultural science classrooms, an ag/mechanics shop, wood shop and classroom, greenhouse, animal lab and outdoor compound. Tennis programs will be conducted at Willowcreek Middle School until the new courts are completed.

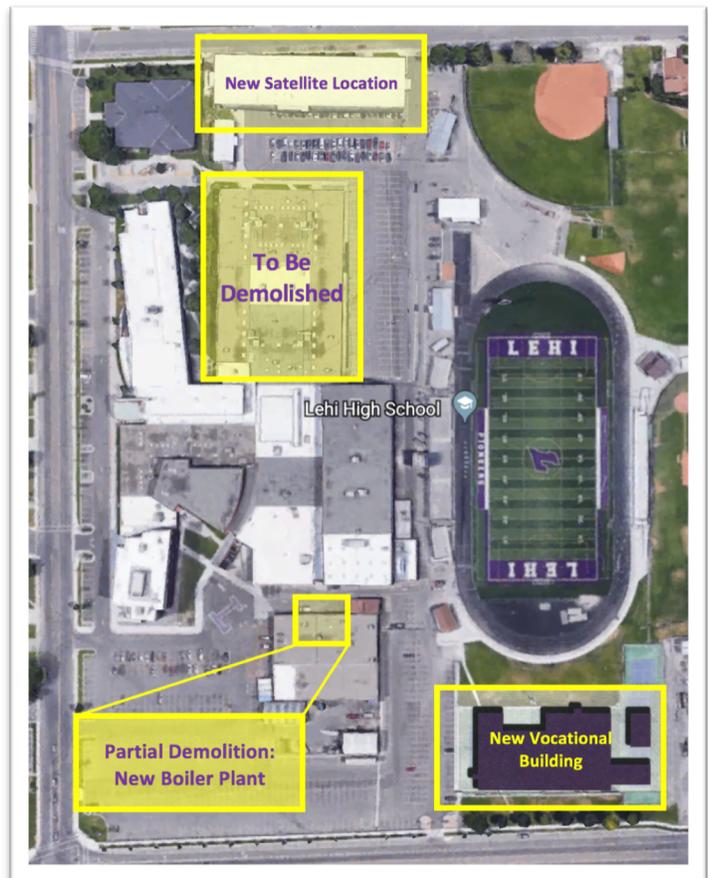

Phase II: This phase will complete demolition of the old vocational building and compound. New construction will include the new main gym, an auxiliary gym, locker rooms and athletics facilities, a three-story classroom wing, and the new auditorium and performing arts classrooms.

Phase III: Phase three will involve the demolition of any remaining portions of the old building including the cafeteria, performing arts hall, and the old athletic wing. Construction will include the second auxiliary gym, commons area/cafeteria, counseling center, media center, and a two-story classroom wing.

Final Site Plan:

